
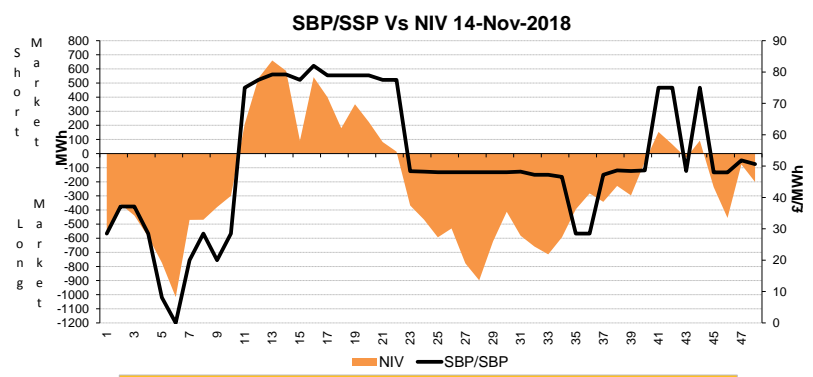
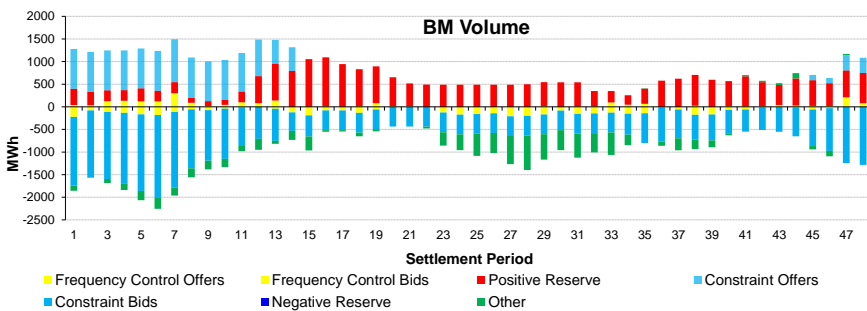
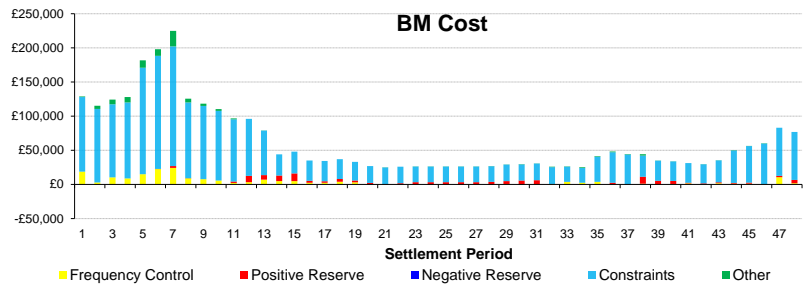



Date: 14/11/2018

BSUoS Charge Estimate: £2.31/MWh
Total Outturn: £3.13m

Daily Balancing Costs



Western Link status: Available

Commentary

300MW of STOR was run for the darkness peak. Additional response was held in the morning for wind volatility and additional response was held in the afternoon for frequency performance risk. ROCOF issues were solved via trades on the Interconnectors and a BM unit in addition to a small number of BM actions. Trades and BM actions were taken to solve power flow restrictions due to planned outages in North of Scotland. BM actions on hydro and wind units were required to solve transmission constraints in Scotland and Northern England. Overnight the voltage levels were regulated with a mix of trades and BM actions.
