






Date: 15/11/2018

BSUoS Charge Estimate: £2.27/MWh  
Total Outturn: £3.22m

# Daily Balancing Costs



■ BM Cost (Indicative)  
■ AS Cost (Estimate)

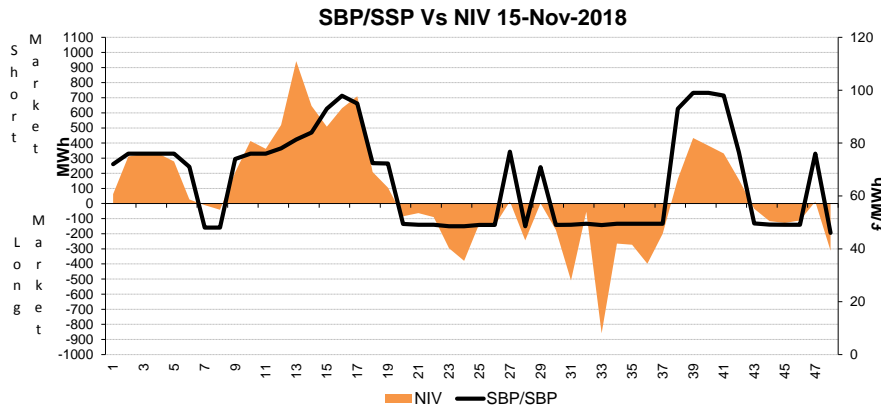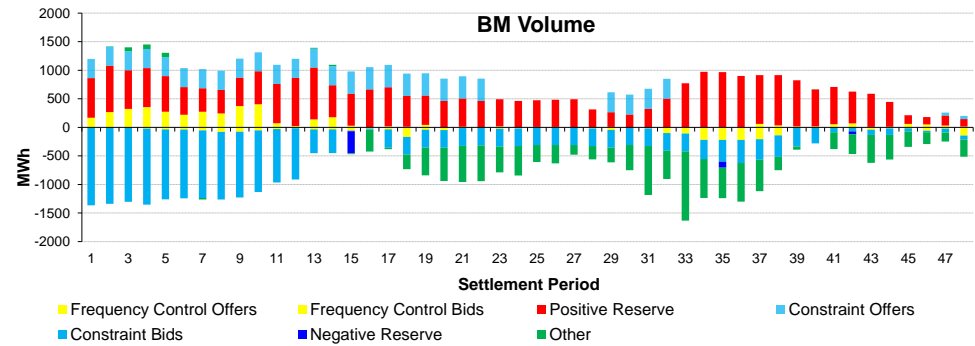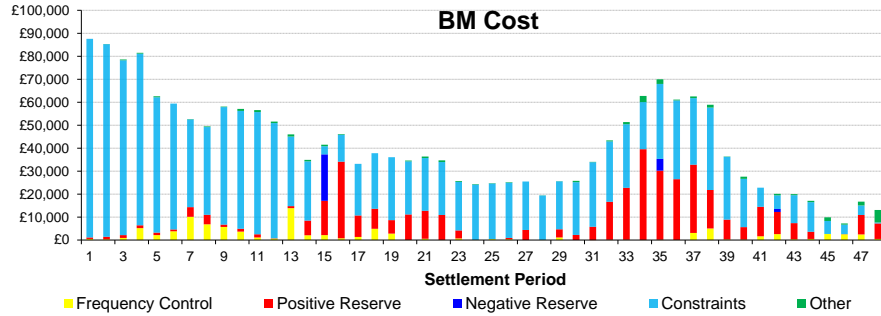

**Western Link status: Available**

## Commentary

800MW of STOR was run over the morning pick up due to wind shortfall and plant loss. Additional high response was held in the run up to the darkness peak due to interconnector swings. RocoF issues were solved via trades on the interconnectors and a BM unit in addition to a small number of BM actions. Trades and BM actions were taken to solve power flow restrictions due to planned outages in North of Scotland and Southern England. BM actions on hydro and wind units were required to solve transmission constraints in Scotland. In addition, trades were taken to manage the voltage levels throughout the country.
