






Date: 17/11/2018

BSUoS Charge Estimate: £1.61/MWh
Total Outturn: £1.82m

Daily Balancing Costs



■ BM Cost (Indicative)
■ AS Cost (Estimate)

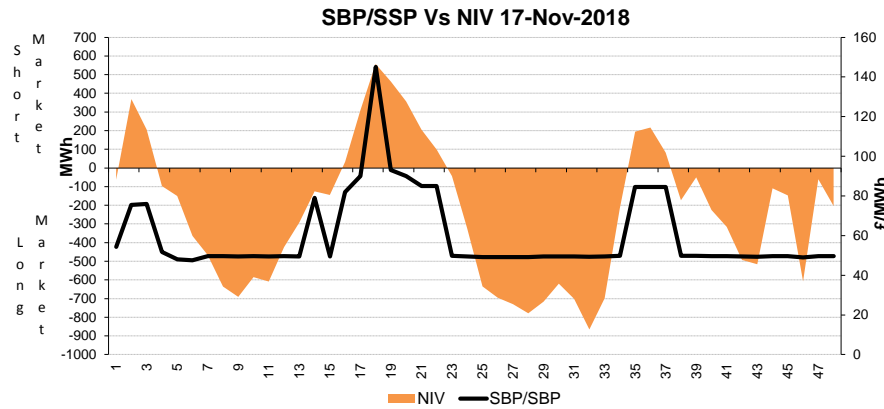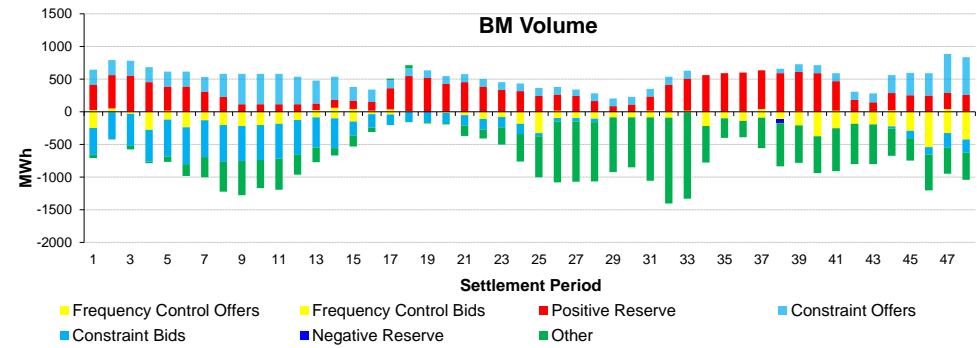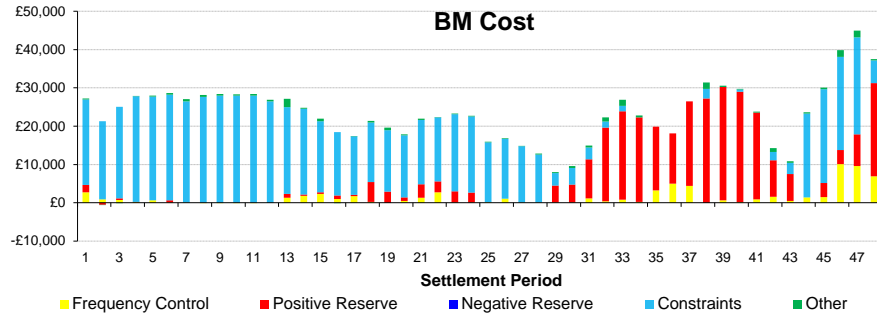

Western Link status: Available

Commentary

150MW of STOR was run in the morning. Additional high response was held in the evening to cover for wind volatility. RocoF issues were solved via trades on the interconnectors and on a BM unit. A small number of BM actions were taken to solve power flow restrictions on the network boundary between England and Scotland in the late evening. Trades and BM actions were taken to manage voltage levels in Scotland and in the North West, North East, South East and South Central regions of England.
