
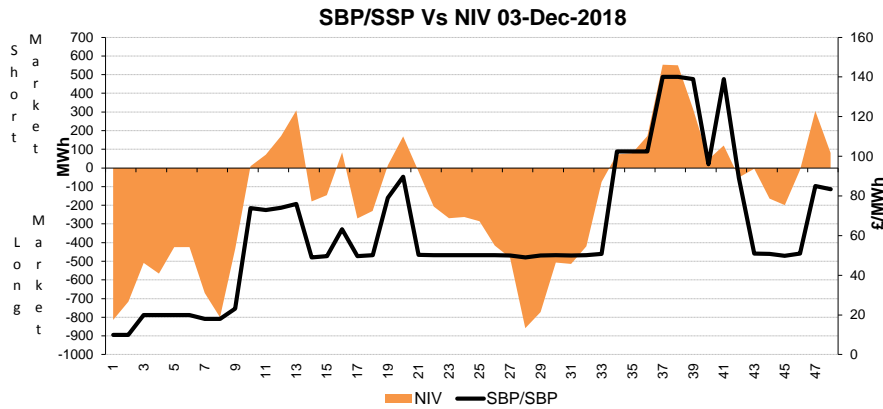
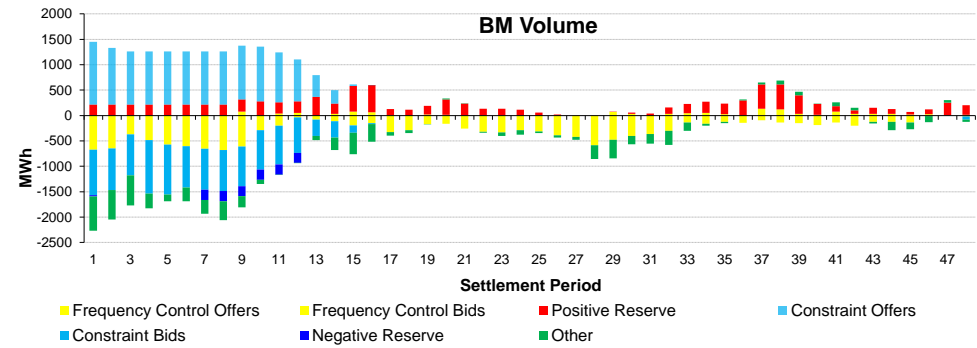
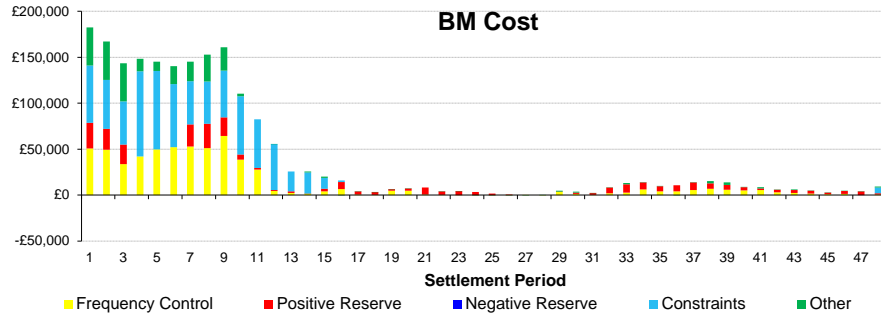



Date: 03/12/2018

BSUoS Charge Estimate: £1.98/MWh  
Total Outturn: £2.84m

# Daily Balancing Costs

BM Cost (Indicative)  
AS Cost (Estimate)



**Western Link status: Available**

## Commentary

Trades were carried out on the Interconnectors for positive margin over the morning peak. During the morning trades were also required for negative reserve. 537MW of STOR was run over the evening peak. Additional dynamic response was held throughout the day. Overnight trades were required on the Interconnectors and on BM units in addition to BM actions for ROCOF. A small number of BM actions were required in the morning on wind and water to manage constraints in Scotland. Trades and BM actions were required for voltage control in the South East, North East, North West, Midlands, South East and Scotland.
