






Date: 22/12/2018

BSUoS Charge Estimate: £2.27/MWh  
Total Outturn: £2.86m

# Daily Balancing Costs



BM Cost (Indicative)  
AS Cost (Estimate)

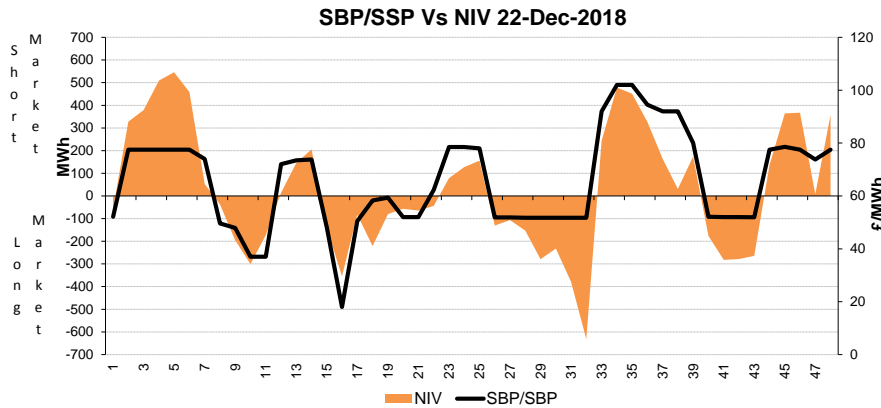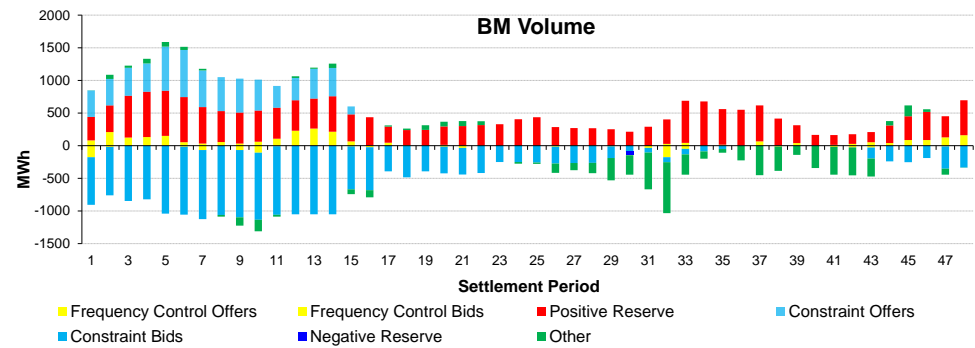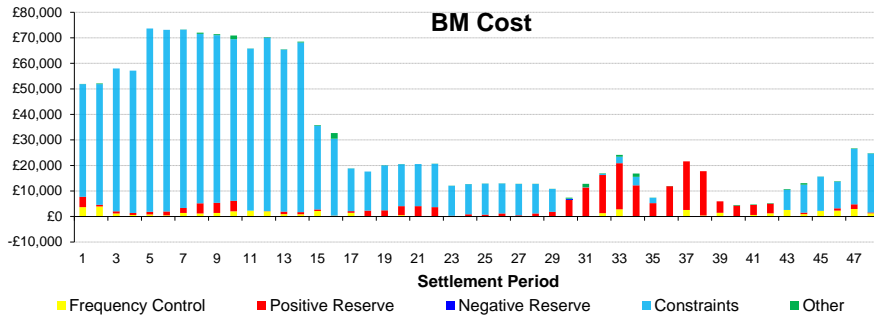

**Western Link status: Available**

## Commentary

Over the evening peak, a BM unit tripped then a synchronising unit also tripped. STOR was used to help cover (~270MW). Some additional units were cancelled as uneconomic and other BM units were kept on instead. Overnight two units were instructed in the BM for voltage support in the Midlands and North West, in addition to a traded unit. ROCOF proved problematic throughout the day; trades were used to solve the majority, particularly overnight on BM units and interconnectors. BM actions were used to solve some ROCOF issues through the rest of the day.
