






Date: 23/12/2018

BSUoS Charge Estimate: £1.81/MWh
Total Outturn: £2.28m

Daily Balancing Costs



BM Cost (Indicative)
AS Cost (Estimate)

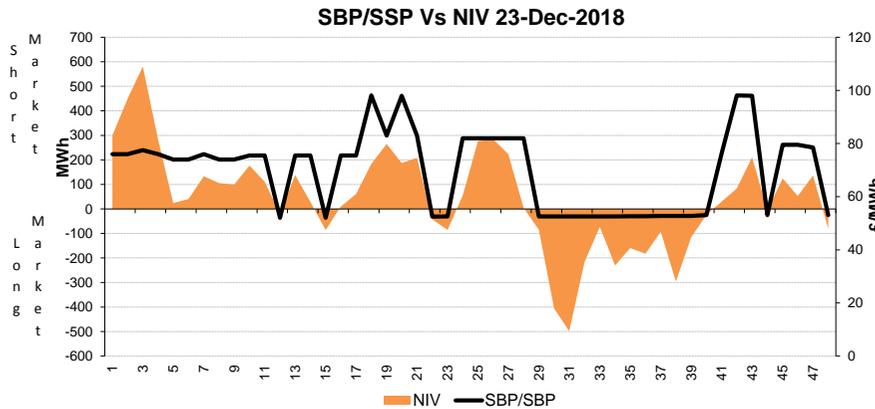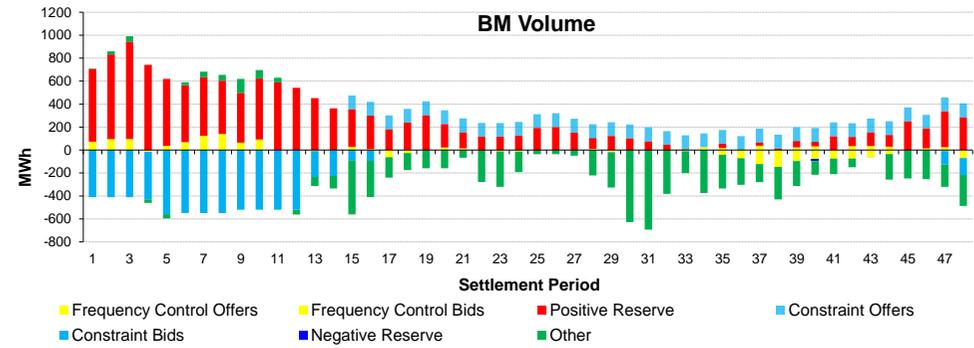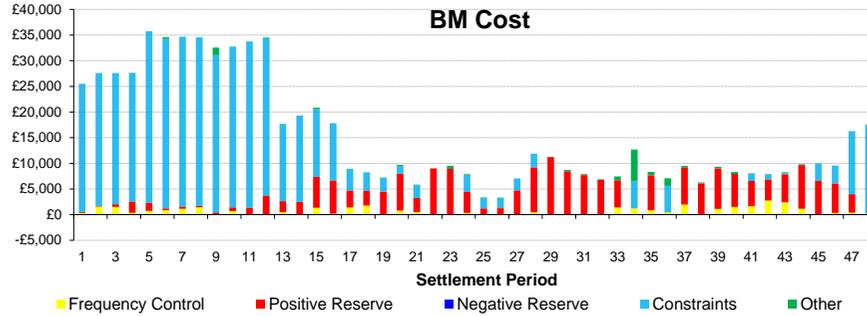

Western Link status: Available

Commentary

During the mid-morning, when the market was short, ~200MW of STOR was instructed which increased to ~300MW by late morning. Just a few BM actions were required for ROCOF, early morning and late evening. Trades were used to further solve ROCOF overnight on BM units and interconnectors. A unit in Scotland was also traded for system security reasons, which further helped resolve a localised constraint in South Scotland.
