
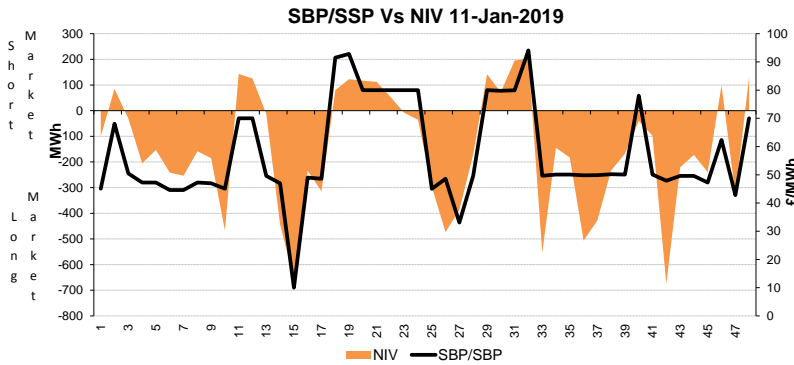
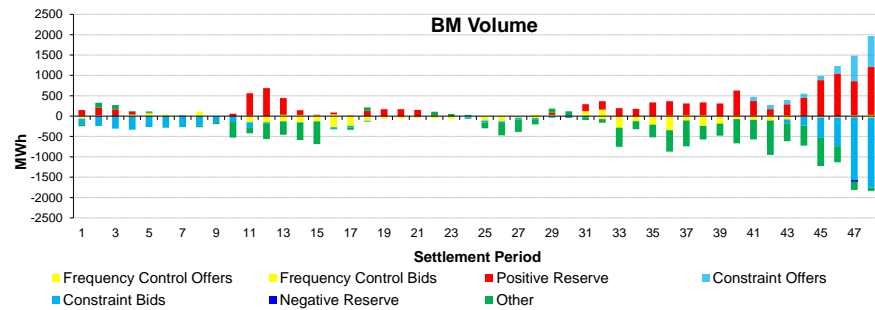
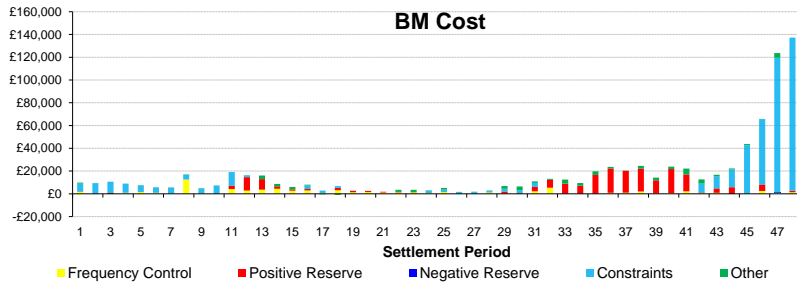



Date: 11/01/2019

BSUoS Charge Estimate: £1.18/MWh
Total Outturn: £1.62m

Daily Balancing Costs



Commentary

Trades were carried out on the interconnectors for positive reserve for the morning pick up along and again through the end of the day. 602MW of STOR was run through the morning and 250MW of STOR was run through the darkness peak. Additional response was held in the morning for wind volatility and in the afternoon for demand uncertainty.

Trades and BM actions were taken overnight to solve ROCOF issues and constraints in the South East. An increase in wind also meant BM actions were required to solve constraints around Scotland and the Scotland England border.

Western Link status: Available
