
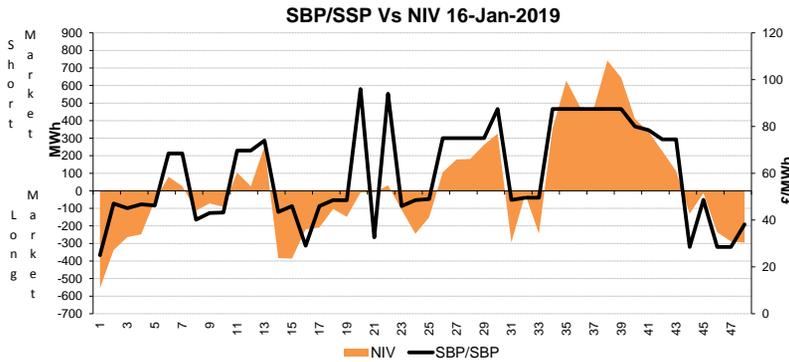
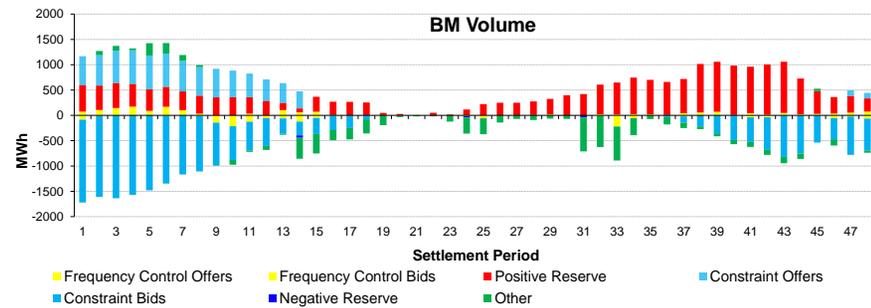
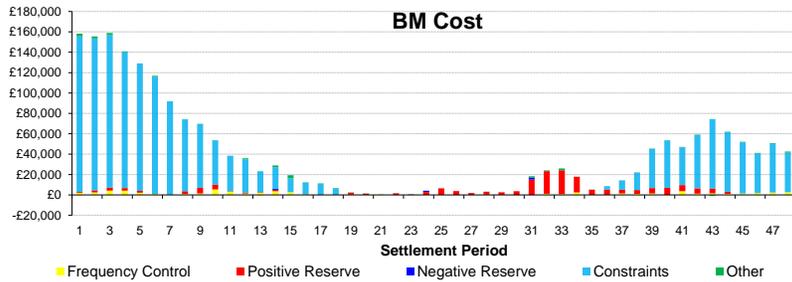


Date: 16/01/2019

BSUoS Charge Estimate: £2.23/MWh
Total Outturn: £3.37m

Daily Balancing Costs



Western Link status: Available

Commentary

Trades were carried out on the interconnectors for positive reserve in order to reduce the interconnector swings around the morning pick up. Demand side STOR was utilised through the morning and then let go as plant came on. Additional response was held across the whole day due to wind volatility. High winds overnight led to BM actions being taken to resolve constraints in Scotland and the Scotland England border. Trades and BM actions were taken to solve ROCOF constraints along with additional BM actions. Trades and BM actions were required to manage voltage levels in the South East, North, North West and the Midlands.
