






Date: Saturday 01 Aug 2020

BSUoS Charge Estimate: £2.75/MWh
Total Outturn: £2.50m

BM Cost (Indicative)
AS Cost (Estimate)



Daily Balancing Costs

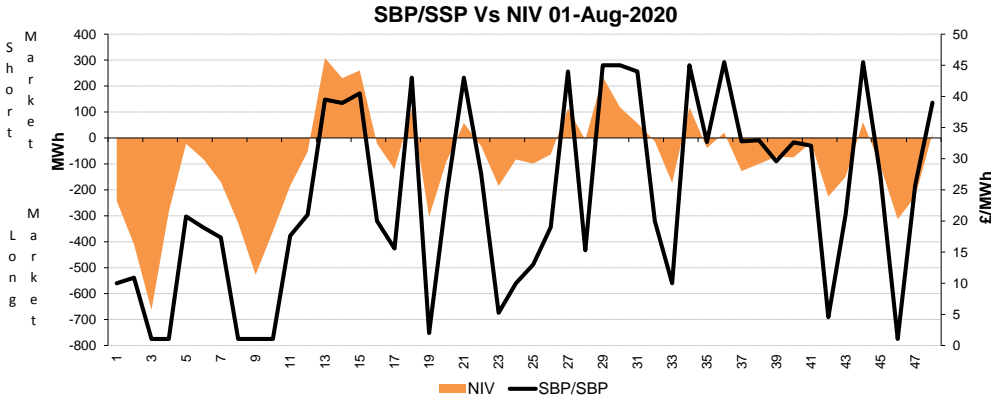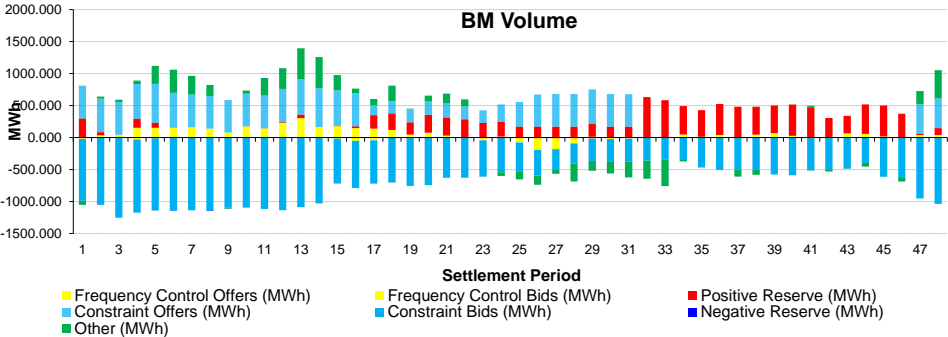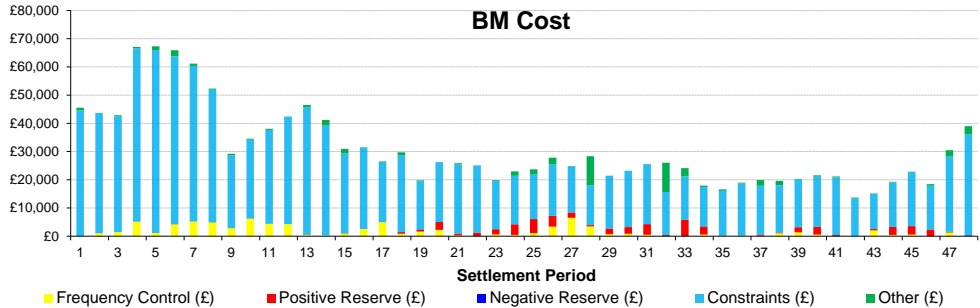

Western Link status: Available

Commentary

The market started off long and then varied through the day. Demand in the afternoon outturned above forecast and 450MW of small BMUs were used. No additional plant was run in the Balancing Mechanism overnight.

Constraints were active on the Scottish border to the relieve thermal constraints. In the morning, high Interconnector flows required BM Actions for RoCoF to increase inertia. Trades were needed in the evening for RoCoF. Trades and BM Actions were used for voltage support.
